




ID	Task Mode	Task Name	% Complete	Duration	Start	Finish	24																
							May	Jun	Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025					
							Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun					
1		PRE-CONSTRUCTION	0%	163 days	Thu 5/23/24	Thu 1/16/25																	
2		100% CD's	0%	1 day	Thu 5/23/24	Thu 5/23/24																	
3		MKS Finalize Bid Packages	0%	5 days	Fri 5/24/24	Fri 5/31/24																	
4		Bid Period	0%	20 days	Fri 5/31/24	Thu 6/27/24																	
5		MKS Recommendation	0%	2 days	Mon 7/1/24	Tue 7/2/24																	
6		School Approval (Signed Contracts)	0%	1 day	Wed 7/17/24	Wed 7/17/24																	
7		Permits	0%	25 days	Fri 5/24/24	Fri 6/28/24																	
8		State Design Release	0%	20 days	Fri 5/24/24	Fri 6/21/24																	
9		Local Building Permit	0%	5 days	Mon 6/24/24	Fri 6/28/24																	
10		Procurement	0%	125 days	Thu 7/18/24	Thu 1/16/25																	
11		Issue Contracts	0%	5 days	Thu 7/18/24	Wed 7/24/24																	
12		Submittals	0%	20 days	Thu 7/25/24	Wed 8/21/24																	
13		Submittal Review	0%	10 days	Thu 8/22/24	Thu 9/5/24																	
14		Long Lead Items	0%	120 days	Thu 7/25/24	Thu 1/16/25																	
15		PEMB	0%	6 mons	Thu 7/25/24	Thu 1/16/25																	
16		Construction	0%	225 days	Thu 8/8/24	Thu 6/26/25																	
17		Mobilize	0%	3 days	Thu 8/8/24	Mon 8/12/24																	
18		Demo	0%	10 days	Mon 8/12/24	Mon 8/26/24																	
19		Site Demo	0%	10 days	Tue 8/13/24	Mon 8/26/24																	
20		Existing School Demo (see below for breakdown)	0%	0 days	Mon 8/12/24	Mon 8/12/24																	
21		Field House Addition	0%	202 days	Tue 8/27/24	Thu 6/12/25																	
22		Sitework	0%	166 days	Tue 8/27/24	Wed 4/23/25																	
23		Site Prep	0%	5 days	Tue 8/27/24	Tue 9/3/24																	
24		Site Utilities	0%	15 days	Wed 9/4/24	Tue 9/24/24																	
25		Site Concrete	0%	15 days	Tue 3/11/25	Mon 3/31/25																	
26		Site Furnishings and Fencing	0%	8 days	Thu 4/10/25	Mon 4/21/25																	
27		Asphalt Patching/Paving/Striping	0%	7 days	Tue 4/1/25	Wed 4/9/25																	
28		Landscaping	0%	5 days	Thu 4/10/25	Wed 4/16/25																	
29		Sitework Complete	0%	1 day	Tue 4/22/25	Tue 4/22/25																	
30		Alt Paving	0%	10 days	Thu 4/10/25	Wed 4/23/25																	
31		Elementry school paving area	0%	10 days	Thu 4/10/25	Wed 4/23/25																	
32		Structural	0%	112 days	Wed 9/4/24	Thu 2/13/25																	
33		Geopier	0%	10 days	Wed 9/4/24	Tue 9/17/24																	
34		Footings	0%	20 days	Wed 9/18/24	Tue 10/15/24																	
35		Foundations	0%	20 days	Wed 10/16/24	Tue 11/12/24																	
36		Load Bearing CMU	0%	30 days	Wed 11/13/24	Mon 12/30/24																	
37		Structural Steel	0%	15 days	Fri 11/29/24	Thu 12/19/24																	
38		PEMB	0%	20 days	Fri 1/17/25	Thu 2/13/25																	
39		Slabs	0%	13 days	Tue 12/31/24	Fri 1/17/25																	
40		Underslab MEP	0%	5 days	Tue 12/31/24	Tue 1/7/25																	
41		Fine Grade	0%	2 days	Wed 1/8/25	Thu 1/9/25																	
42		Prep SOG Pour 1	0%	2 days	Fri 1/10/25	Mon 1/13/25																	
43		Pour SOG Pour 1	0%	1 day	Tue 1/14/25	Tue 1/14/25																	
44		Prep SOG Pour 2	0%	2 days	Wed 1/15/25	Thu 1/16/25																	

Project: Fieldhouse Schedule
Date: Thu 5/30/24

Task		Summary		Manual Summary Rollup		Manual Progress
Split		Project Summary		Manual Summary		
Milestone		Manual Task		Progress		



ID	Task Mode	Task Name	% Complete	Duration	Start	Finish	Schedule												
							24	May	Jun	Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025
							Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	
45		Pour SOG Pour 2	0%	1 day	Fri 1/17/25	Fri 1/17/25													
46		Envelope	0%	89 days	Wed 11/13/24	Mon 3/24/25													
47		Brick Veneer	0%	20 days	Fri 2/14/25	Thu 3/13/25													
48		Metal Siding	0%	15 days	Fri 2/21/25	Thu 3/13/25													
49		Roofing/Curbs	0%	15 days	Fri 2/21/25	Thu 3/13/25													
50		Gutters	0%	5 days	Fri 3/14/25	Thu 3/20/25													
51		Windows	0%	3 days	Fri 2/14/25	Tue 2/18/25													
52		Storefront	0%	5 days	Fri 3/14/25	Thu 3/20/25													
53		Doors and Frames	0%	30 days	Wed 11/13/24	Mon 12/30/24													
54		Tie in to existing building complete	0%	1 day	Fri 3/21/25	Fri 3/21/25													
55		Weather Tight	0%	1 day	Mon 3/24/25	Mon 3/24/25													
56		Interior (includes common area A001)	0%	85 days	Fri 2/14/25	Thu 6/12/25													
57		Non load bearing CMU	0%	20 days	Fri 2/14/25	Thu 3/13/25													
58		Door Frames	0%	20 days	Fri 2/14/25	Thu 3/13/25													
59		In Wall MEPs	0%	20 days	Fri 2/14/25	Thu 3/13/25													
60		In Wall Inspections	0%	1 day	Fri 3/14/25	Fri 3/14/25													
61		Above Ceiling MEPFP	0%	20 days	Fri 3/14/25	Thu 4/10/25													
62		Install ceiling grid/perimeter tile	0%	15 days	Fri 4/11/25	Thu 5/1/25													
63		Above Ceiling Inspections	0%	1 day	Fri 5/2/25	Fri 5/2/25													
64		Install remaining ceiling tile	0%	8 days	Mon 5/5/25	Wed 5/14/25													
65		Paint 1st coat	0%	10 days	Mon 3/17/25	Fri 3/28/25													
66		Paint 2nd coat	0%	10 days	Fri 5/2/25	Thu 5/15/25													
67		Paint Ceiling and Exposed MEPFP Gymnasium	0%	8 days	Mon 5/5/25	Wed 5/14/25													
68		Install sports flooring	0%	10 days	Thu 5/15/25	Wed 5/28/25													
69		Striping in Gymnasium	0%	5 days	Thu 5/29/25	Wed 6/4/25													
70		Flooring	0%	13 days	Mon 5/12/25	Wed 5/28/25													
71		Base	0%	13 days	Mon 5/12/25	Wed 5/28/25													
72		Toilet Partitions	0%	8 days	Fri 5/16/25	Tue 5/27/25													
73		Toilet Accessories	0%	5 days	Wed 5/28/25	Tue 6/3/25													
74		MEP Trimout	0%	10 days	Fri 5/16/25	Thu 5/29/25													
75		Final Inspection	0%	5 days	Thu 6/5/25	Wed 6/11/25													
76		Interior Addition Complete	0%	1 day	Thu 6/12/25	Thu 6/12/25													
77		Existing School Remodel	0%	179 days	Tue 8/13/24	Mon 4/28/25													
78		Install temp protection	0%	1 day	Tue 8/13/24	Tue 8/13/24													
79		Demo exterior	0%	5 days	Tue 8/13/24	Mon 8/19/24													
80		Install shoring to support wall/roof above wall to be demolish	0%	2 days	Wed 8/14/24	Thu 8/15/24													
81		Demo Existing Storefront	0%	3 days	Fri 8/16/24	Tue 8/20/24													
82		Demo Existing Lockers, Showers, etc.	0%	10 days	Fri 8/16/24	Thu 8/29/24													
83		Install New Storefront System	0%	15 days	Mon 9/23/24	Fri 10/11/24													
84		Final Inspections	0%	3 days	Mon 10/14/24	Wed 10/16/24													
85		Existing School Remodel Complete	0%	1 day	Thu 10/17/24	Thu 10/17/24													
86		Pool	0%	26 days	Mon 3/24/25	Mon 4/28/25													
87		Install temp protection	0%	1 day	Mon 3/24/25	Mon 3/24/25													
88		Drain Pool	0%	3 days	Tue 3/25/25	Thu 3/27/25													

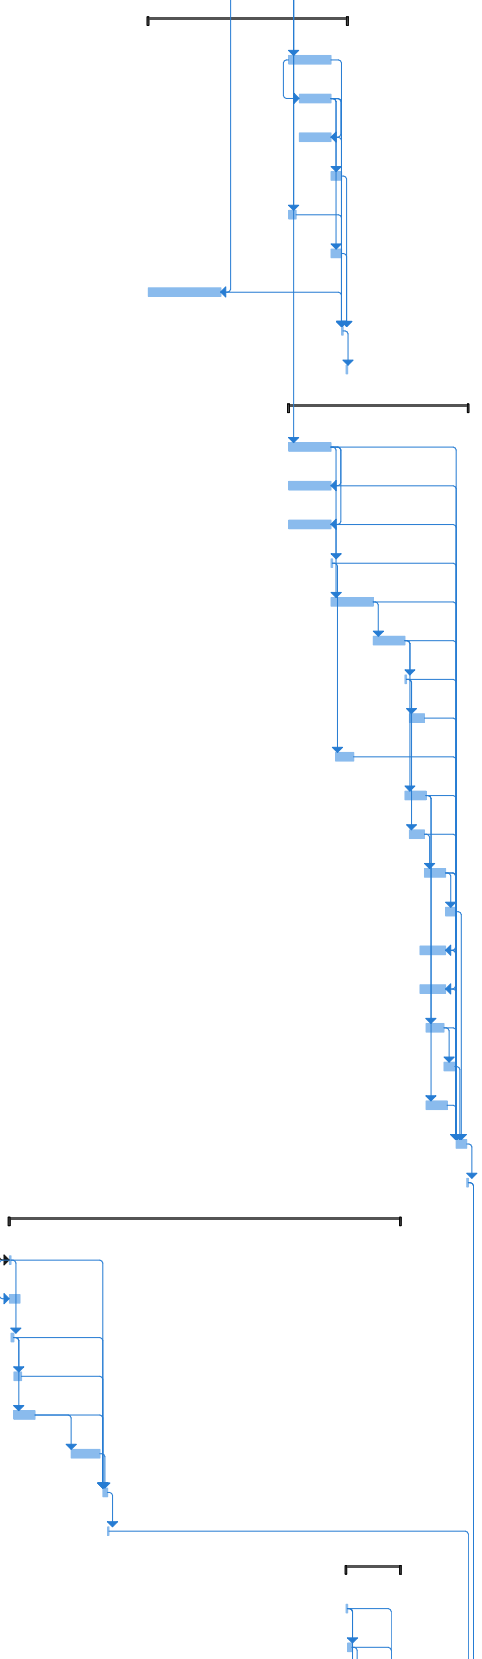

Project: Fieldhouse Schedule
Date: Thu 5/30/24

Legend for Gantt chart symbols:

- Task: Blue bar
- Split: Dotted line
- Milestone: Diamond
- Summary: Thick black bar
- Project Summary: Thin black bar
- Manual Task: Blue bar with black outline
- Manual Summary Rollup: Thick black bar with black outline
- Manual Summary: Thin black bar with black outline
- Progress: Blue bar with black outline
- Manual Progress: Blue bar with black outline and arrow



ID	Task Mode	Task Name	% Complete	Duration	Start	Finish	24															
							May	Jun	Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025				
							Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun				
89		Demo Pool Gutter, Liner and Pipe Connections	0%	4 days	Fri 3/28/25	Wed 4/2/25																
90		Install new Perimeter Gutter	0%	5 days	Thu 4/3/25	Wed 4/9/25																
91		Install new liner	0%	3 days	Thu 4/10/25	Mon 4/14/25																
92		Demo Slab for foundation prep	0%	2 days	Tue 3/25/25	Wed 3/26/25																
93		Pour new foundation	0%	2 days	Thu 3/27/25	Fri 3/28/25																
94		Set Steel	0%	10 days	Wed 4/9/25	Tue 4/22/25																
95		Demo Rooftop Equipment	0%	2 days	Tue 3/25/25	Wed 3/26/25																
96		Demo Mechanical Equipment	0%	4 days	Thu 3/27/25	Tue 4/1/25																
97		Set new Rooftop Unit	0%	3 days	Thu 3/27/25	Mon 3/31/25																
98		Install New Mechanical Equipment	0%	8 days	Tue 4/1/25	Thu 4/10/25																
99		Final Inspections	0%	3 days	Wed 4/23/25	Fri 4/25/25																
100		Pool Complete	0%	1 day	Mon 4/28/25	Mon 4/28/25																
101		Closeout	0%	10 days	Fri 6/13/25	Thu 6/26/25																
102		Punch List	0%	10 days	Fri 6/13/25	Thu 6/26/25																
103		Owner Training	0%	2 days	Fri 6/13/25	Mon 6/16/25																
104		COC	0%	5 days	Fri 6/13/25	Thu 6/19/25																
105		Turnover	0%	1 day	Fri 6/20/25	Fri 6/20/25																

Project: Fieldhouse Schedule
Date: Thu 5/30/24

Task		Summary		Manual Summary Rollup		Manual Progress
Split		Project Summary		Manual Summary		
Milestone		Manual Task		Progress		

Page 3
